


# Trail's Edge Weekly Update



## TRAIL'S **TE** EDGE — APARTMENTS —

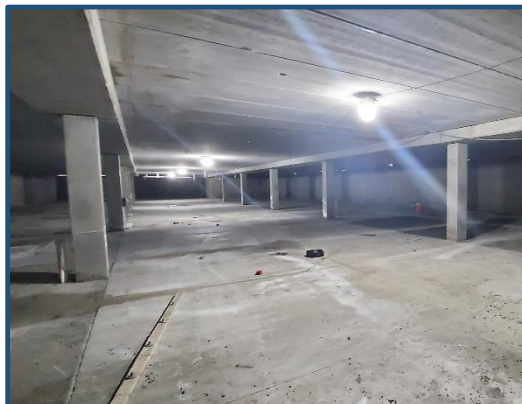

### Progress Since Last Update:

- Roof trusses have been installed.
- Roof decking is currently being installed.
- The garage floor continues to be poured.
- MEP rough-in is currently taking place on 1<sup>st</sup> and 2<sup>nd</sup> floor.

### Anticipated Progress in the Next Three Weeks:

- Garage floor will be completed.
- Roof decking will be complete, and roofing will begin.
- Phase (2) 1<sup>st</sup> floor wall panels will be set.
- Phase (1) windows and patio doors will be delivered.



<b>Today's Date:</b>	9/3/2021
<b>Start Date:</b>	3/19/2021
<b>Completion Date:</b>	2022
<b>% Completed:</b>	25%
<b>On Track for Completion Date:</b>	Yes
<b>Days lost to poor weather:</b>	0 of 5
<b>Architect:</b>	Scott Kintopf
<b>Project Manager:</b>	Ryan Weyker
